




PdM Solutions of San Antonio, Inc

THERMOGRAPHIC REPORT

Date:	8-20-2001	Contract #:	XXXXXXXX
COMPANY NAME:	XXXX	LOCATION:	San Antonio, Texas
ADDRESS:	XXXX	EQUIPMENT ID:	C3-Starter Soft Starter
CITY, STATE ZIP:	XXXXX	SEVERITY:	PROBLEM

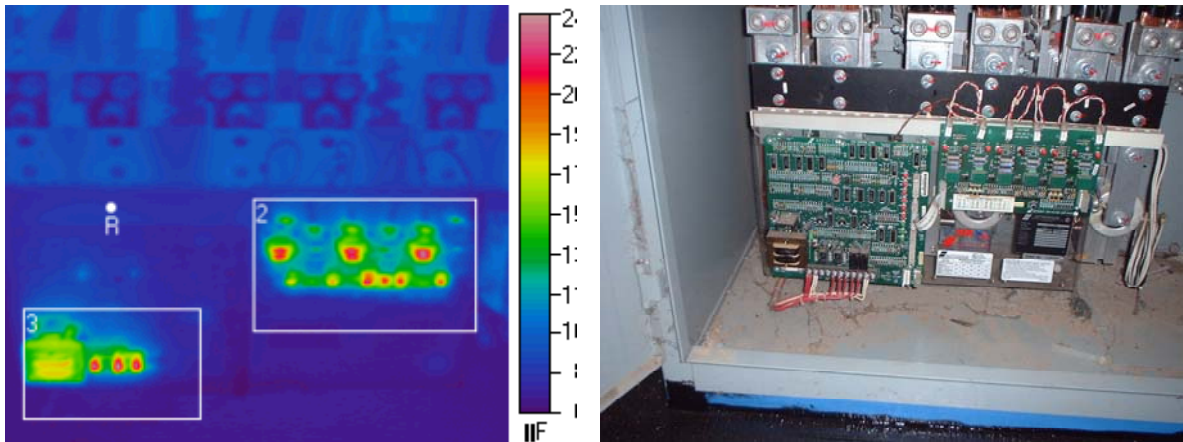

	Ref.	Rect2	Rect3
Emiss.	0.970	0.970	0.970
Avg °F		110.7	105.9
Min °F		73.0	71.3
Max °F	86.1	243.7	251.2
Delta °F		158.7	166.1

PROBLEM:	Over heated starter control board
RECOMMENDATION:	Temporarily install cooling fans. Contact factory for permanent solution
INSPECTOR:	XXXXXXXX
ASSISTANT:	Non
CORRECTIVE ACTION TAKEN:	Will install cooling fans
